

2nd Work Report

(April 30, 2026 to July 24, 2026)

construction of one building holding 2 classrooms, an office, storage space, and restrooms for the Public Preschool of Adjigo Governorate of Atokolibé Municipality of Banté Republic of Benin

As soon as the roof was finished, the plastering work began. The sand was sifted. Doors and shutters were installed.



Then the bricklayers began plastering the building. They started at the inside of the classrooms.




The blackboards were installed.

Then the exterior walls were plastered.



Next, the soils were compacted and cemented.

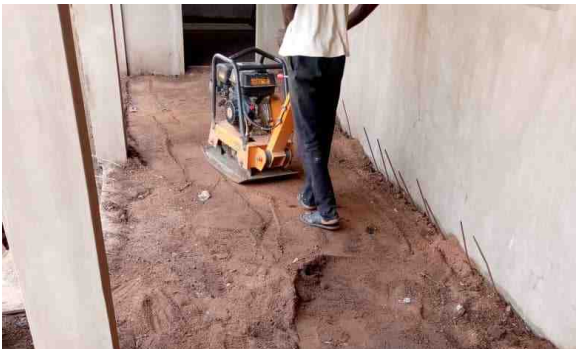

An iron reinforcement was installed in the veranda floor. After cementing, the floors were treated with a studded roller.



The ramp railing was installed. The steps were cemented.



The burglar protection was installed.




Finally, the roof ridge was closed.



The toilet pit was finally ready and could be lined with bricks.



The walls were plastered with Sikalite and Sikalutex and sealed.

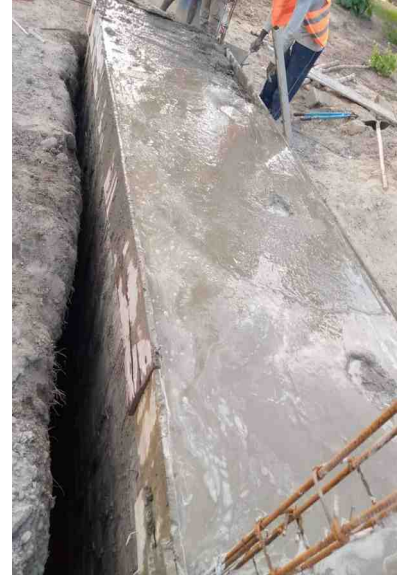

The toilet block was then built on top of that.



The plaster had to dry for a month before the painters could begin their work.

Finally on June 24th the painters arrived. The walls were scrubbed.



After the first coat of paint was applied, the building slowly became colorful.



The rooms also became lively.




The toilet block was painted



And finally, the murals are finished.





The logos were also painted.



The opening ceremony will be postponed until the end of September, as there are school holidays until mid-September.
I thank all my friends from the bottom of my heart, and especially a friend from Bavaria, for their support.
Astrid Toda
