

2nd Work Report
(March 15 to May 18, 2026)

**Construction of one building holding 2 classrooms, an office,
storage space, and toilets
for the Public Preschool of Kadolassi
Badjoudè County
Municipality of Ouaké
Republic of Benin**

Once the roof was made, our bricklayers returned to Kadolassi to begin the plastering work. The doors and shutters were installed first.




Meanwhile, the apprentices sifted the sand.



First, the interior of the rooms were plastered.



The blackboards were laid out.

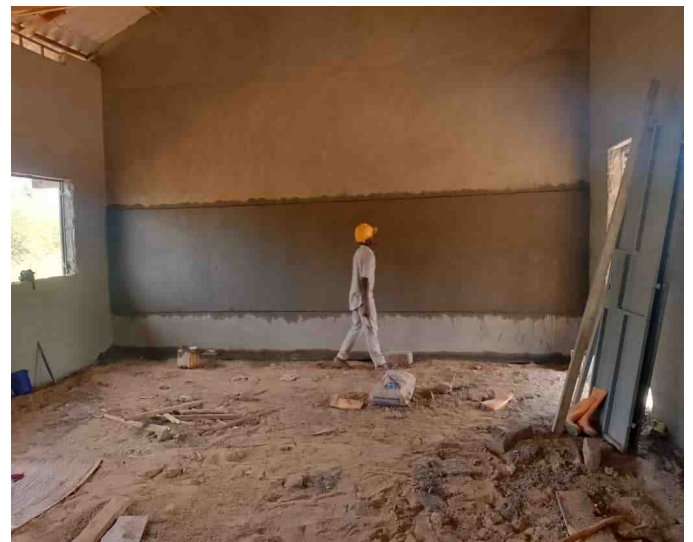

The women carried water to the construction site.



After the interior was finished, the exterior walls were plastered.



The railing of the ramp was placed and the protective walls for the building's foundation were built.




The soils were then soaked with water, compacted, and cemented.



An iron reinforcement was embedded in the floor of the veranda and, after the concrete was poured, treated with a studded roller. This is an attempt to prevent fine cracks in the concrete.



The toilet block was also plastered. At times our construction team worked under floodlights.

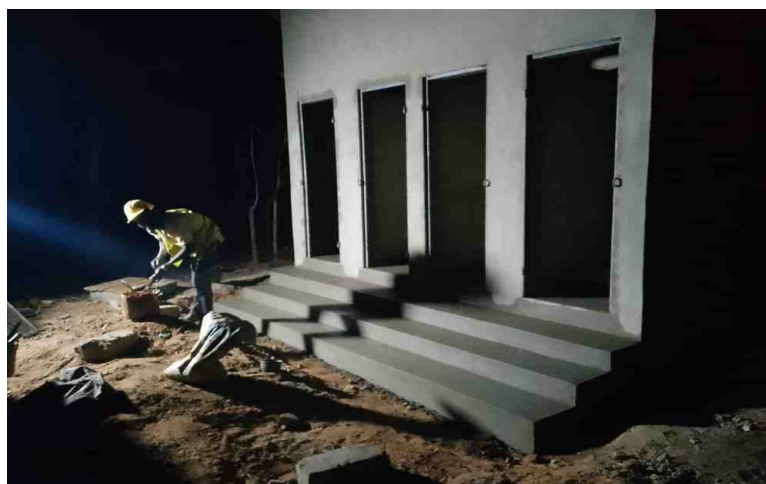

The ventilation pipes were installed.



The masonry work is complete.



Three weeks later, the painters arrived at the construction site. In a very short time, the appearance of the new preschool building changed.



The artists designed the interior of the classrooms.





There's lots for the children to see.
And finally, everything is finished. Even the logos are painted on.



The children are overjoyed. They can hardly wait until June 10th when they can finally move into their new rooms.

We sincerely thank all the supporters who made this project possible. If the donor or employees of Fly and Help would like to attend the opening ceremony, we would be absolutely delighted.

Warm regards
Astrid Toda
