

2nd work report
(22. March 2026 to 31. July 2026)

**construction of a building holding 4 classrooms, an office, a
storage room, and toilets
for the public preschool of Wakou Tebo
Governorate of Oroukayo
Municipality of Kouandé
Republic of Benin**

The macons returned to the construction site and first of all installed the doors and shutters. Then the plastering work began.



First the interior of the rooms was plastered, then the exterior.



The railing of the ramp was also installed.

Finally, the floors were cemented.



Meanwhile, some macons were working on the toilet block.




The foundation for the water tower was poured and the pillars were incorporated into it.





The tower grew taller with strong iron supports. The water reservoirs were installed.

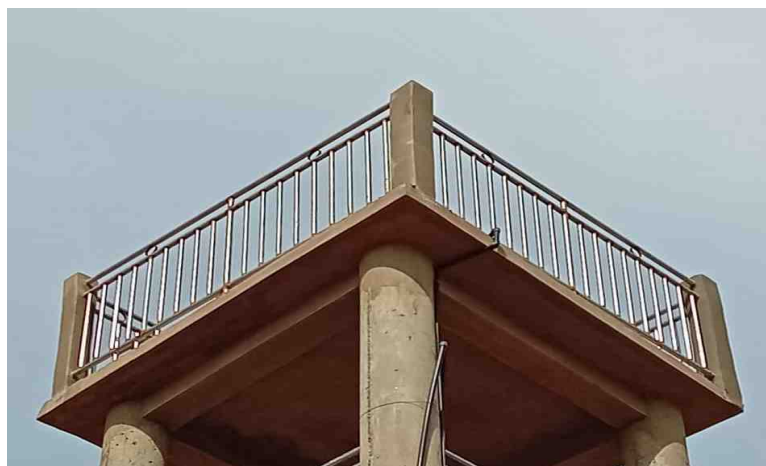

The railings were installed.



The water tower was protected from intruders.

The water taps have been built.



After a one-month drying period, the painters arrived.



In just a few days, the school changed its appearance.



The toilet block was also painted. Each cubicle was given a different color.



Finally, the logos were painted.



We thank all our friends and supporters who have consistently stood by us, and the new friends we have just met. The project in Wakou Tebo is the northernmost project we have undertaken in Benin. A few years ago, we built a school building in the desert sands of the Niger. The northern regions have their own customs and laws. It was an honor to be welcomed into their community. The cooperation and friendship have deeply touched us. I send a heartfelt "thank you" to Wakou Tebo.

The opening ceremony will take place at the beginning of the new school year.

From my heart

Astrid Toda
